## **RRV 12 MONTHLY INSPECTION FORM**

Examine / Check / Test each item listed below (use machine specific service manual & maintenance plan for information regarding inspection procedures and criteria). Indicate in the appropriate space below as each item has been performed. If the item is not found acceptable, describe each discrepancy in the comment space on the rear. Take immediate action to correct all discrepancies or remove machine from service.


Confirm Maintenance Plan Used

Case SPMM 0001 Iss 2	Dozer SPMM 0006 Iss 3	Dumper SPMM 0003 Iss 1	TD12 SPMM0005 Iss 2	
Case SPMM 0001 Iss 3	CX135 SPMM 0004 Iss 1	✓ PC128 SPMM 0010 Iss 1		
Giga SPMM 0007 Iss 2	Evo MEWP SPMM 0011 Iss	s1		

Cur	ent Hours 3504	Plant Number	CX 198	
Mac	hine Make & Type CASE CX135	Serial Number	DCH 1300198	
Item	Inspection / Check Detail		Result X - ✓ -	- N/A
	All pre start checks			V
	Grease and lubricate as per maintenance plan			1
	All fluid levels correct, hydraulic, batteries, brake etc. Check for			/
	Hydraulic cylinders, pivot pins, pivot points and hoses - Examir	ne		
	Steering locks - Check			NIA
	Trailer park brake pressure - Test			
	Service brake filter element - Renew			NIA
	Brake system general - Check			~
	Service brake - Test ( 3 dynamic tests or pull tests or torque hu	ıb test)		
	Service brake pressure - Test			1
	Rail wheel brake system - Examine			V
	Parking brake - Test			i
	Wheel nuts - Check			V
_	Rail wheels - Check / Examine			/
	Rail wheels back to back - Check measurements ( 1358 - 1363	)		~
	Rail wheel bearings - Check (spin / lift test)			
	Rail wheel bearings - Examine if fault found during spin / lift tes	t		
_	18 Traction hubs - Check		NIA	
	19 Road wheels and tyres - Examine		NIA	
	20 Tyres to rail wheel interface - Examine and confirm squeeze measurement - 18 - 25mm		NIA	
	Rail bogie / axle pivots and trunnion - Examine			V
	Rail bogies / axles - Examine			~
	Rail axle interlocks - Test ( adjust if required )			WIN
	Dozer front bogie / trolley - Check			NiA
	Dozer front bogie / trolley brake pads - Check			NIA
	26 Dozer front bogie / trolley brake - Check		NIA	
	Emergency recovery system operation - Test			V
	28 Operation of all lights - Check / Examine		X	
	Operation of horn - Check / Test			
	Glass and wipers - Check Safety labels - Check			
	Recovery tow bar and hitches condition and security - Check			V
	Inderframe and super structure - components and welds - Che	ck		
	Slew locks - Check	CK		-
		acord results on l	AET form and attach	V ./
	35 Rated capacity indicator - Test and complete data download ( record results on LAFT form and attach ) 36 Visibility of paintwork and overall appearance, including yellow panels. Check			
	Wisibility of paintwork and overall appearance, including yellow panels - Check  Trailer brake away siren - Test			V
	38 Electrical components / connections / wiring - Check			
	39 Ballast weight - Check			
	40 Earth bond cables - Test and Examine			
	41 Check valves - Check			
	ire extinguisher - Examine			1
1.				V

Item	Inspection / Check Detail Result X - ✓ -	N/A
43	LOLER cert / lifting accessories and safety devices - Check	
	Auxiliary lifting point/s (if fitted) and decals - Examine	
	Quick hitch - Examine if fitted	MIL
	Machine cab file - Check	
	Tracks / running gear - Check	V 100
48	ALO device / Duel height limiter - Test and Examine	MIM
49	Rail head scrapers - Examine	1
50	Overload sounders - Check	V
51	Camera system - Check	MIN
52	Basket and harness points - Examine	AIG
53	Torque hub brake adaptors - Examine	Ain
54		<u> </u>

Record details of three stopping distances on chart below. If any recording differ by 10% from the previous test then investigate / retest. If any recordings are in the fail section investigate and then retest. Adverse track conditions can affect recording but must be deatiled / recoreded accordingly. Chart data derived from RIS 1530 PLT.

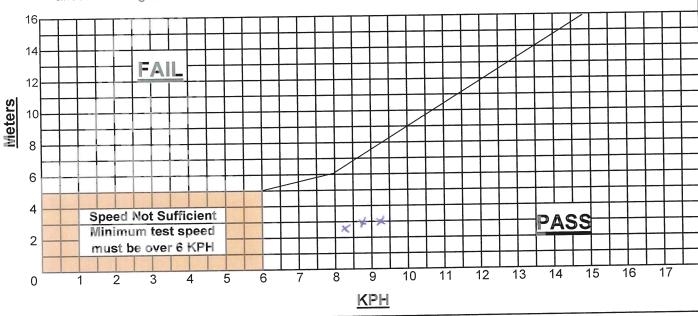

0/5/F Boom work nor- Replaces.
AUX LIFT POINT IN GOOD ORDER.
Brakes TESTED AS PER SORVICE PLAN

MACHINE IN GOOD ORDGE

Comments / Additional Work - Checks

I certify the above checks / examinations have been conducted and any corrective actions required have been completed and recorded.					
Signed Signed					
Print D. SCHORELD	Date completed	10.1.17-			
