

# RRV 12 MONTHLY INSPECTION FORM

Examine / Check / Test each item listed below (use machine specific service manual & maintenance plan for information regarding inspection procedures and criteria). Indicate in the appropriate space below as each item has been performed. If the item is not found acceptable, describe each discrepancy in the comment space on the rear. Take immediate action to correct all discrepancies or remove machine from service.

Confirm Maintenance Plan Used

Giga SPMM 0007 Iss 2	Case SPMM 0001 Iss 4 / 5	924 AJH 146 Shovlin Iss3	Valtra RMQ60080V01 Iss 2
Giga ZM50005083 Iss 2	✓ Case SPMM 0001 Iss 6 / 7	924 HMM0015 Iss E	
	TD12 SPMM0005 Iss 3 / 4	Evo MEWP SPMM 011 Iss2	


Current Hours	5560	Plant Number	2227
Machine Make & Type	TEREX GIGA	Serial Number	1805301286

Item	Inspection / Check Detail	Result X - ✓ - N/A
1	All pre start checks	✓
2	Grease and lubricate as per maintenance plan	✓
3	All fluid levels correct, hydraulic, batteries, brake etc. Check for leaks.	✓
4	Hydraulic cylinders, pivot pins, pivot points and hoses - Examine	✓
5	Steering locks - Check	✓
6	Trailer park brake pressure - Check/record pressure 60bar	✓
7	Service brake filter element - Renew	✓
8	Brake system general - Check ROAD BRAKE TEST PASSED 1.9m.	✓
9	Service brake - Test ( 3 dynamic tests or pull tests or torque hub test)	✓
10	Service brake pressure - Check/record pressure 100 bar	✓
11	Rail wheel brake system - Examine	✓
12	Parking brake - Test	✓
13	Wheel nuts - Check	✓
14	Rail wheels - Check / Examine Complete SP WIRS 01	✓
15	Rail wheels back to back - Check measurements ( 1358 - 1363 )	✓
16	Rail wheel bearings - Check (spin / lift test)	✓
17	Rail wheel bearings - Examine if fault found during spin / lift test	✓
18	Traction hubs - Check	✓
19	Road wheels and tyres - Examine	✓
20	Tyres to rail wheel interface-Examine	✓
21	Rail bogie / axle pivots and trunnion - Examine	✓
22	Rail bogies / axles - Examine	✓
23	Rail axle interlocks - Test ( adjust if required )	✓
24	Dozer front bogie / trolley - Check	N/A
25	Dozer front bogie / trolley brake pads - Check	N/A
26	Dozer front bogie / trolley brake - Check	N/A
27	Emergency recovery system operation - Test	✓
28	Operation of all lights - Check / Examine	✓
29	Operation of horn - Check / Test Complete Horn and RCI Sounder Test Results Sheet SP-HT 01	✓
30	Glass and wipers - Check	✓
31	Safety labels - Check	✓
32	Recovery tow bar and hitches condition and security - Check	✓
33	Underframe and super structure - components and welds - Check	✓
34	Slew locks - Check	✓
35	Rated capacity indicator - Test and complete data download ( record results on LAFT form and attach )	✓
36	Visibility of paintwork and overall appearance, including yellow panels - Check	✓
37	Trailer brake away siren - Test	✓
38	Electrical components / connections / wiring - Check	✓
39	Ballast weight - Check	✓
40	Earth bond cables - Test and Examine using Resistance Ohmmeter 622424	✓
41	Check valves - Check	✓
42	Fire extinguisher - Examine	✓



Item	Inspection / Check Detail	Result X - ✓ - N/A
43	LOLER cert / lifting accessories and safety devices - Check	✓
44	Auxiliary lifting point/s (if fitted) and decals - Examine	✓
45	Quick hitch - Examine if fitted	✓
46	Machine cab file - Check	✓
47	Tracks / running gear - Check	N/A
48	ALO device / Dwell height limiter - Test and Examine	✓
49	Rail head scrapers - Examine	✓
50	Overload sounders - Check Complete Horn and RCI Sounder Test Results Sheet SP-HT 01	✓
51	Camera system - Check	✓
52	Basket and harness points - Examine	N/A
53	Torque hub brake adaptors - Examine	✓
54	Air Brake Pressure Check - Record Pressure	✓

Record details of Static Brake Test torque test readings for Service Brake (SB) and Park Brake (PB) per wheel or alternatively, if conducting on track testing, of three stopping distances on chart below. If any recording differs by 10% from the previous test then investigate / retest. If any recordings are in the fail section investigate and then retest. Adverse track conditions can affect recording but must be detailed / recorded accordingly. Chart data derived from RIS

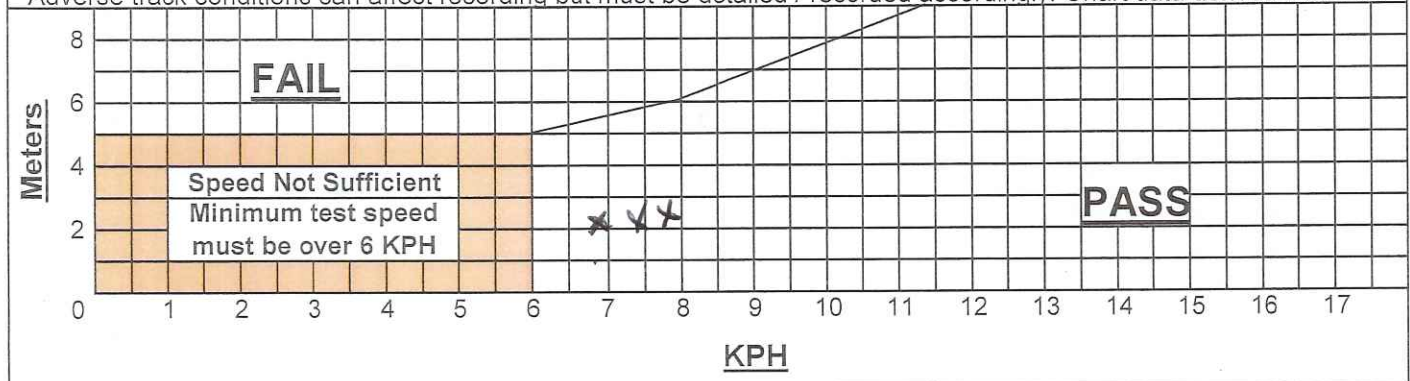

**CALIBRATED TOOLS USED**

Type	Serial Number	Date
HYD CLOCK	34128566	15.12.24
MICRA MICRA	622424	10.5.24

**Comments / Additional Work - Checks**

**EARTH BOND TEST RESULTS**

Dipper End to Left Rail 0.817mΩ  
 Dipper End to Right Rail 0.5312mΩ

BRAKES TESTED AS PER SERVICE PLAN  
 AUX LIFT POINT IN GOOD ORDER  
 MACHINE IN GOOD ORDER.  
 DRAW BAR PULL TEST - PASSED 3600kg

I certify the above checks / examinations have been conducted and any corrective actions required have been completed and recorded.

Signed 

Print D. Scuderi

Date completed 16.04.24

# SHOVLIN PLANT

HIRE LIMITED

## RAIL WHEEL BRAKING TORQUE TEST

Date:	16.04.24		
Machine:	TEREX GIGA ROLLER		
Serial No:	1205301286	Location:	YARD
Plant No:	2227	Hours:	5360

Inspection Point	Inspection Limits	Pass	Fail
Brake Pad Wear	Minimum 3mm	✓	
Brake Pad Damage	None allowed	✓	
Contamination	None allowed	✓	
Brake Pad Adjustment	1mm	✓	
Floating Pins	Clean and lubricate with graphite grease	✓	
Hydraulic Hoses / Fittings	Check for damage / leaks	✓	
Brake Disc Protection	Check for damage / security	✓	
Brake Discs	Check for damage / security	✓	
Fixing / Fasteners	Check for damage / security	✓	
Torque limits	See back of sheet for required limits		

**For AJH brake systems, refer to AJH097 for torque test requirements**

**Where OEM torque test figures are not available, the following should be used:**

**Park Brake (Nm) =  $\frac{\text{Machine Weight (Kg)}}{20}$**  Minimum Park brake required:

**Service Brake (Nm) =  $\frac{\text{Machine Weight (Kg)}}{10}$**  Minimum Service brake required:

Equipment to be used:	GIGA ROLLER	ID No:	130086	Cal Exp Date:	4.12.24
Equipment to be used:	TORQUE PUMP	ID No:	741167896836	Cal Exp Date:	30.11.24

Park Brake: 1350Nm  
Service Brake: 2370Nm  
Pass / Fail **PASS**

FRONT

REAR

Park Brake: 1350Nm  
Service Brake: 2370Nm  
Pass / Fail **PASS**

Park Brake: 1350Nm  
Service Brake: 2370Nm  
Pass / Fail **PASS**

Park Brake: 1350Nm  
Service Brake: 2370Nm  
Pass / Fail **PASS**

As the engineer responsible for executing this testing, I confirm that I have used calibrated equipment and had the relevant training. Prevailing weather conditions did not affect the outcome of this test.

Engineer: D. Scovelin	Signed: <i>[Signature]</i>
-----------------------	----------------------------

As an Approver of Shovlin Plant I confirm that this inspection/test was executed by a suitably qualified service engineer.

Approver: Jacob Shovlin	Signed: <i>[Signature]</i>
-------------------------	----------------------------

# SHOVLIN PLANT

HIRE LIMITED

## RAIL WHEEL BRAKING TORQUE TEST

### Torque Limits

	Park Brake (Nm)	Service Brake (Nm)
Case 988	1350Nm	1684Nm
Giga Railer	1330Nm	2362Nm
Liebherr	1250Nm	2500Nm

	Park Brake (kgF)	Service Brake (kgF)
TD12-1512	1480 kgF	2970 kgF
Other TD12s	1000 kgF	1600kgF
